


Task	Description	Predecessor	Duration (days)
A	Requirements Analysis	-	2
B	Feature Definition	A	2
C	Backend Setup	B	3
D	Database & Migration	C	4
E	API Development	D	4
F	Frontend Setup	B	3
G	UI Development	F	5
H	Feature Implementation	G	4
I	System Integration	E, H	3
J	Testing & Bug Fixing	I	4
K	Deployment	J	1

The table above presents the PERT analysis of the project, including task dependencies and estimated durations.

Each task is defined with a fixed duration (deterministic approach), and dependencies indicate the order of execution. Tasks E and H converge into the integration phase, after which testing and deployment are performed.

This structure reflects a real-world software development workflow with parallel frontend and backend development.

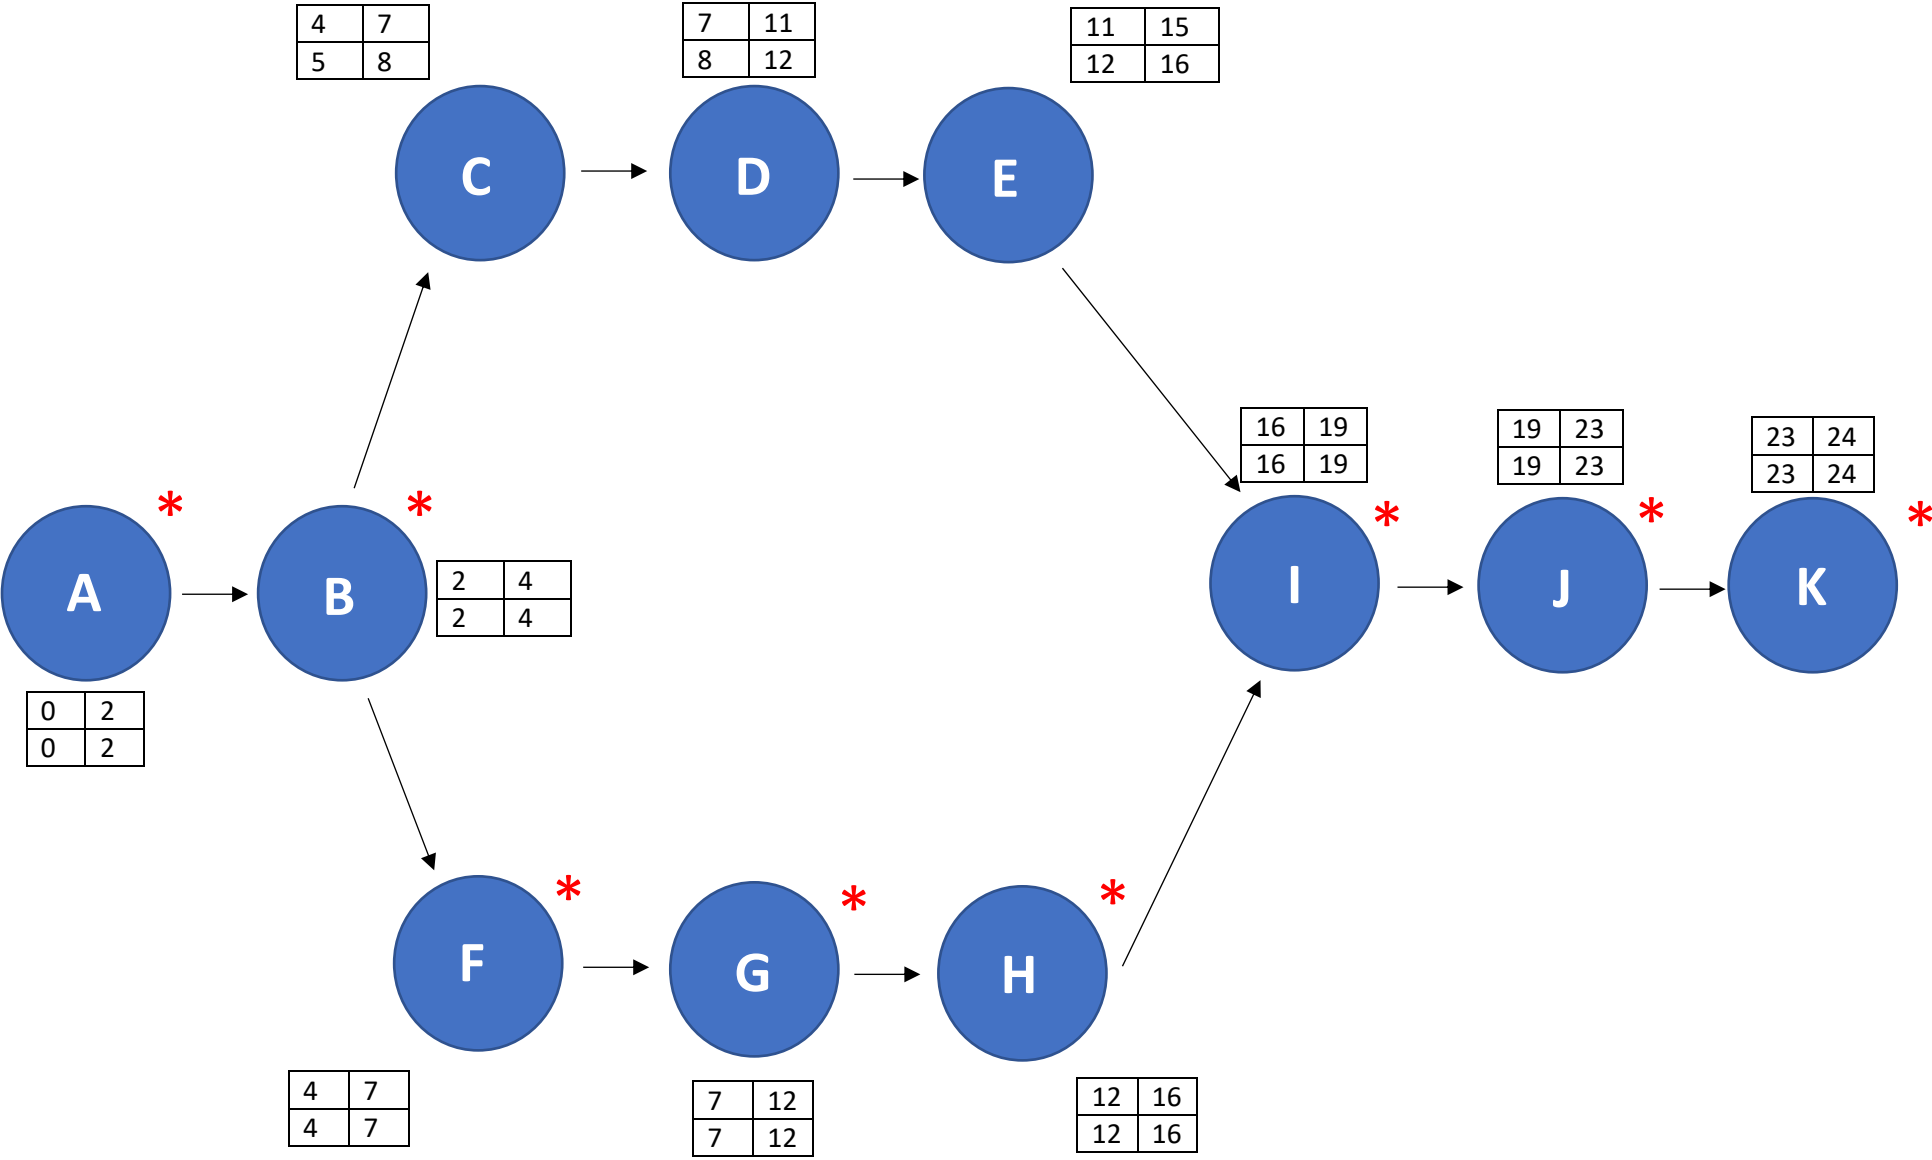

Based on the PERT diagram analysis, the critical path is A – B – F – G – H – I – J – K, resulting in a total project duration of 24 days. Activities on this path have zero slack, meaning any delay will directly affect the project completion time.
